

ROAD PAINTING (ROAD MARKINGS, SIGNAGES)



Name of Contractor

**Kataline Infra
Products Ltd**



Project Consultant

Swaraj Engineering Services



Estimated Cost

Rs 8.465 Cr



Accepted Tender
percentage

4.13% below



Present Status of
Work

95% completed



Payment Made

Rs 5.96 Cr.



Date of
Commencement
09/08/2019



Third Party
Supervision

CEIL



Maintenance
period


5 years after completion



Reasons for Delay

**Covid Pandemic
Rainfall**



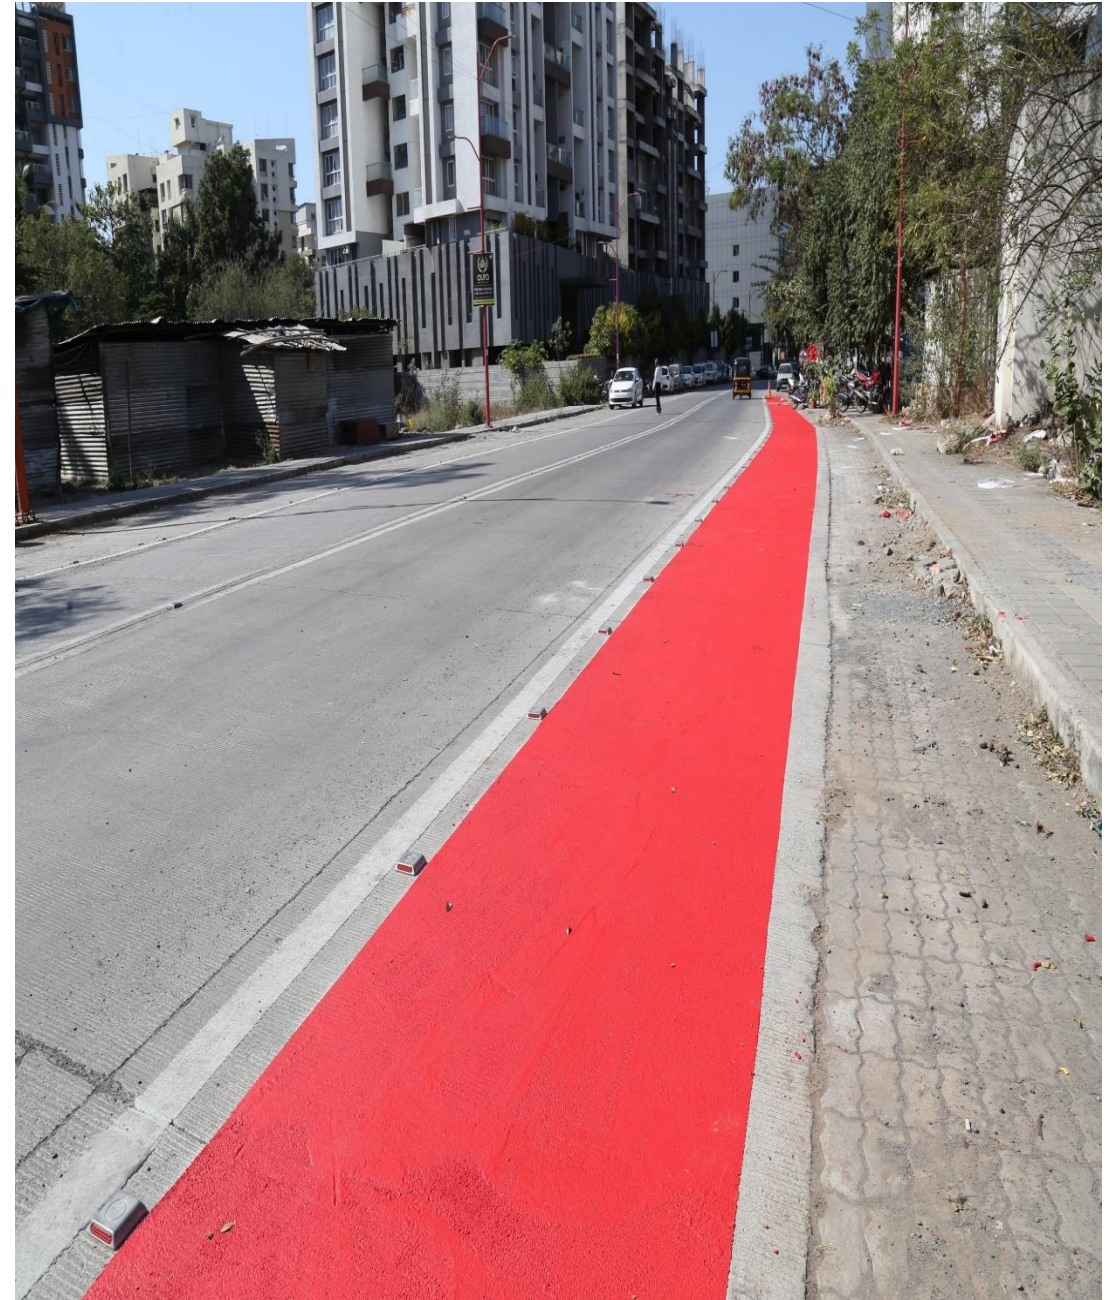

Latitude: 18.578919
Longitude: 73.769475
Elevation: 569.05±3 m
Accuracy: 3.1 m
Azimuth: 243° (SW)
Pitch: -1.2° (1.0°)
Time: 20-05-2022 11:38

Powered by AngleCam

