

SWIMMING POOL

S.NO
153+154+155,
BANER



Swimming Pool



Location

Northern Side of
Jupiter Hospital



LOA Amt

Rs. 1.23Cr



Total Amt Paid

Rs 1.23Cr



Accepted Tender

8.87 % Below



Area of Plot

1614.85 sqm



Date of
commencement

06/03/2019



Date of Completion

31/12/2019

(Handed over to Sports Dept,
PMC)



Project Architect

Vishwas Bhat



Third Party
Supervision

CEIL



DLP period of 2
years up to

31/12/2021



Objective

Completion of PMC
incomplete project

COMPLETING CONSTRUCTION OF A PARTLY BUILT SWIMMING POOL AT 153+154+155, BANER

Change Room and Washroom

1. Completion of remaining Brick Works
2. Provision of floor and wall tiles
3. All plumbing works including plumbing and sanitary fittings.
4. All electrical work including provision of light fittings
5. Internal and external Painting


General works

1. Provision of PVC doors and fittings
2. Provision of aluminum shutter to all Window
3. Provision main entrance wooden Door
4. Provision brick work and plaster for Garden Flower Bed.
5. Provision of Cafeteria
6. Security Surveillance work (4 CCTV work).
7. Extension of compound wall
8. 20 KVA DG Set
9. Outdoor lighting (10 Street lights)

Handover

Project has been handed over to Sports dept, PMC after completion of the project.



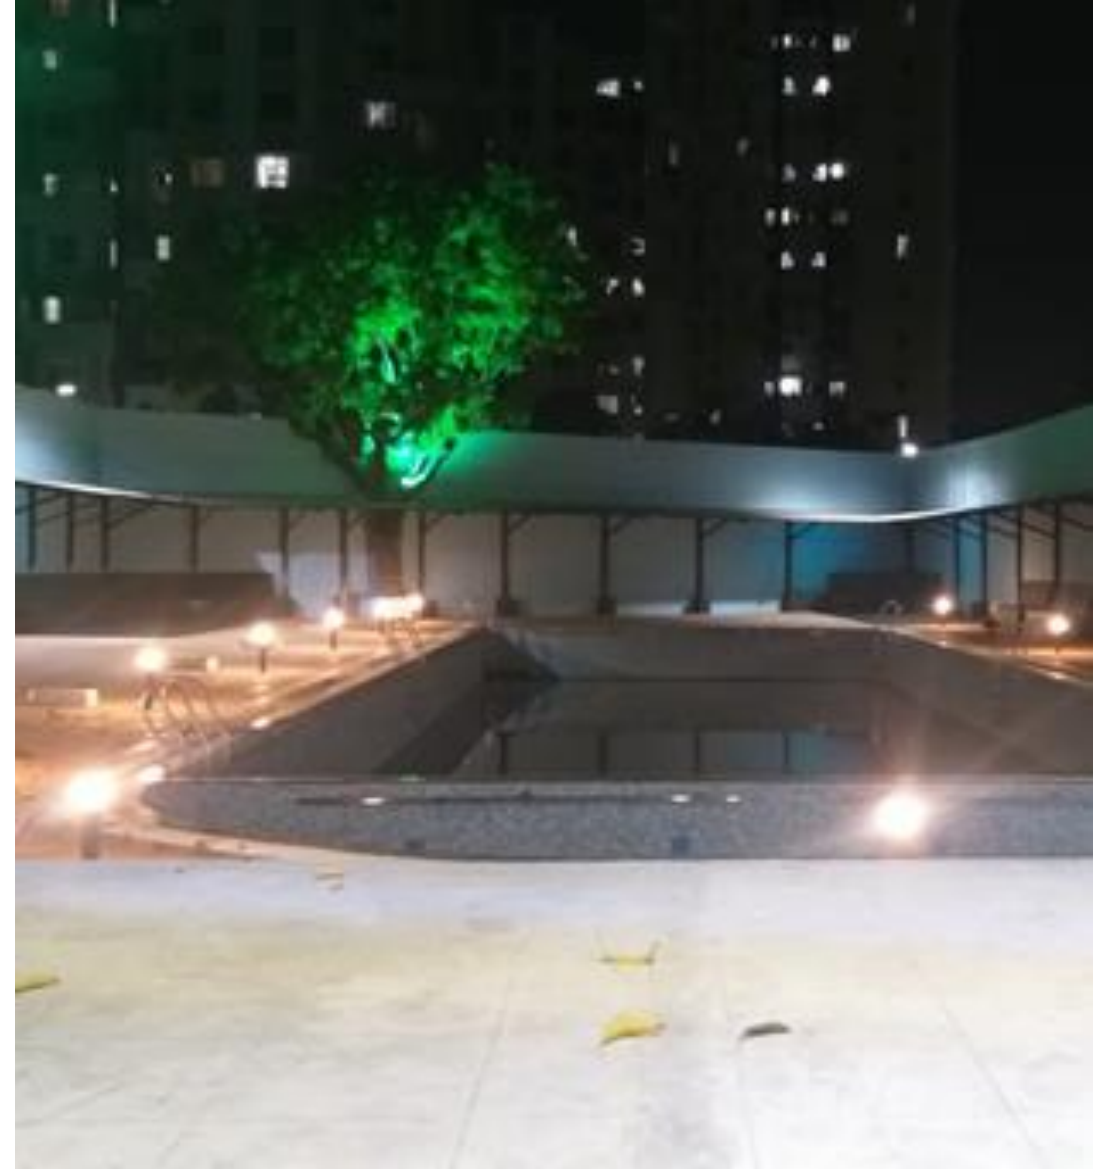

NIGHT VIEW OF COMPLETED WORK
